



# Arlington High School Building Project

AHS Construction Update – 11/17/2022

## Arlington HS Construction Schedule: April 2020 – September 2025

### Construction Details

Phase 1 construction is complete and the new Performing Arts and Science, Technology, Engineering, Arts & Mathematics wings are open. Phase 2 began immediately after the Phase 1 building turnover. Part of the old school has been demolished and that area is closed off from the existing school during the next phase of construction.

### COVID-19 Update


The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates  
<https://ahsbuilding.org/news/construction-updates/>  
 For more information, visit:  
[www.ahsbuilding.org](http://www.ahsbuilding.org)  
 Email questions or concerns to:  
[ahsbuilding@arlington.k12.ma.us](mailto:ahsbuilding@arlington.k12.ma.us)

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative, (617) 352-8593



### PHASE 2 BUILDING CONSTRUCTION (February 2022 – September 2023)

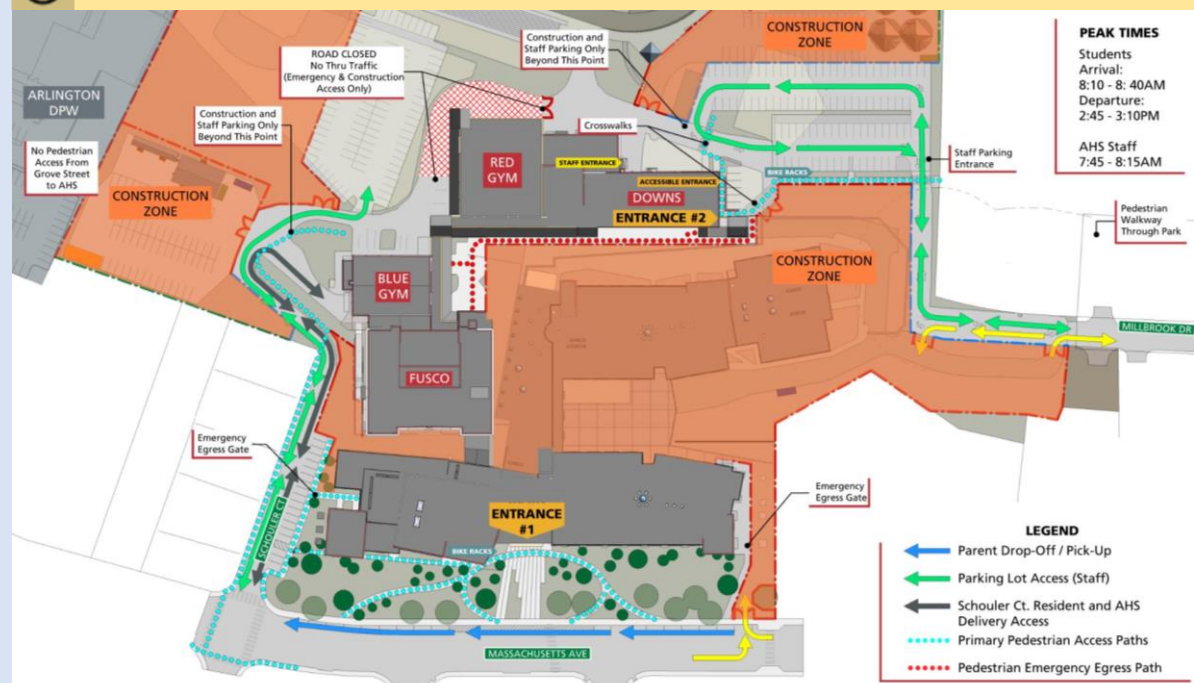

**PEAK TIMES**  
 Students  
 Arrival: 8:10 - 8:40AM  
 Departure: 2:45 - 3:10PM  
 AHS Staff  
 7:45 - 8:15AM

### Construction Look Ahead – Week of November 21<sup>st</sup>, 2022

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

#### Public Way Impacts:

- Deliveries/demo debris trucking ongoing

#### General Site Activities:

- Phase 2:
  - Steel erection and metal decking installation
  - Steel and concrete deliveries
  - Steel fireproofing
  - Concrete placement
  - Exterior metal stud framing
  - Dust mitigation ongoing
- Phase 1 Building Closeout:
  - Temporary rope fence installed to protect grass growth
- West Parking Lot (adjacent to DPW):
  - Construction trailers and contractor parking
- Material Stockpile/Temp Construction Lot:
  - Contractor storage and parking
- Schouler Court:
  - Construction vehicles entering and exiting project site

#### Weekend Work/Holiday Work/Night Work:

- Saturday work is required for the foreseeable future
- There is no work on Thanksgiving Day



Skanska USA Inc.  
 Owner's Project Manager



Consigli Construction Co., Inc.  
 Construction Manager at Risk



HMFH Architects, Inc.  
 Architect





CONSIGLI  
*Est. 1905*


## ARLINGTON HIGH SCHOOL

### WEEKLY UPDATE – WEEK OF NOVEMBER 21<sup>ST</sup>, 2022

#### Progress Photographs



*Photograph 1: Phase 2 East Elevation (View from Mill Brook Drive) - Taken Week of 11/14/2022*

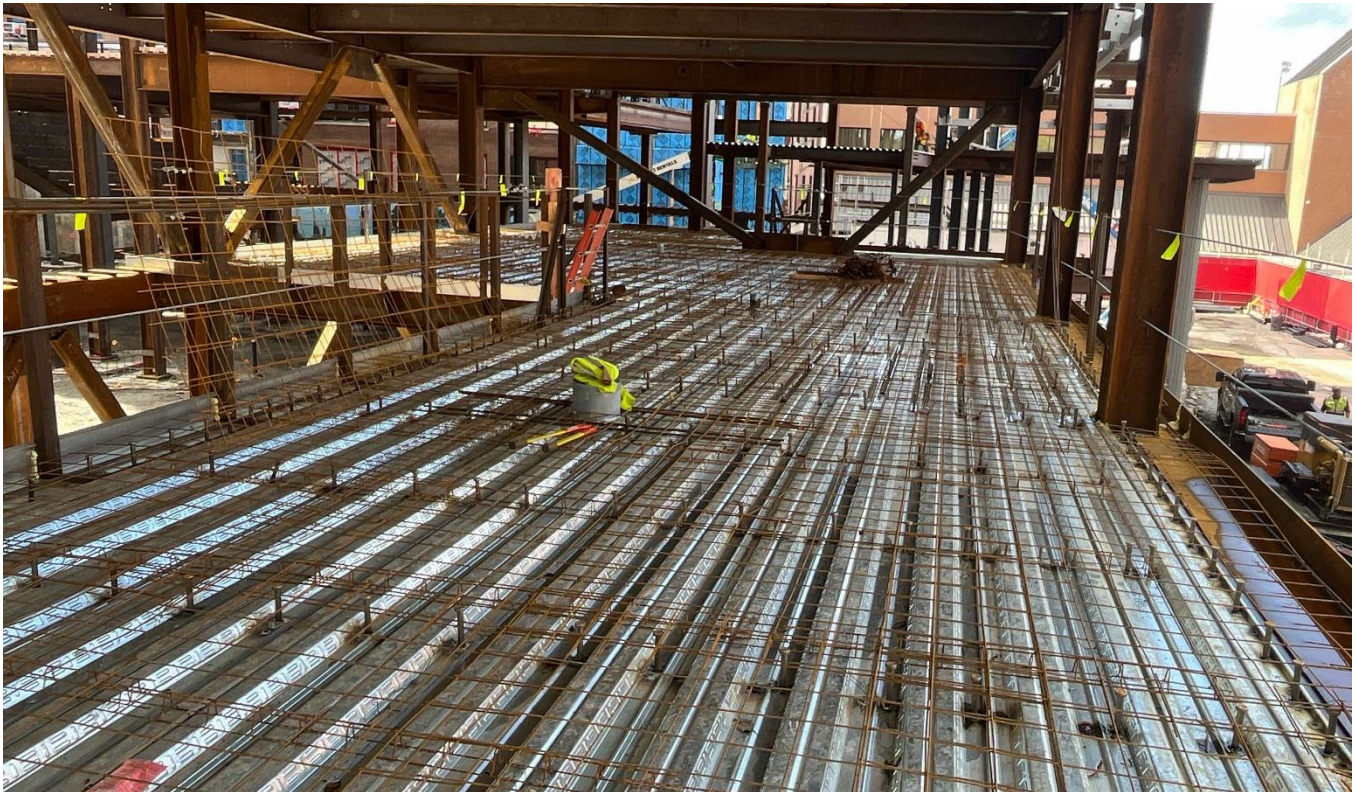

*Photograph 2: Metal decking*
